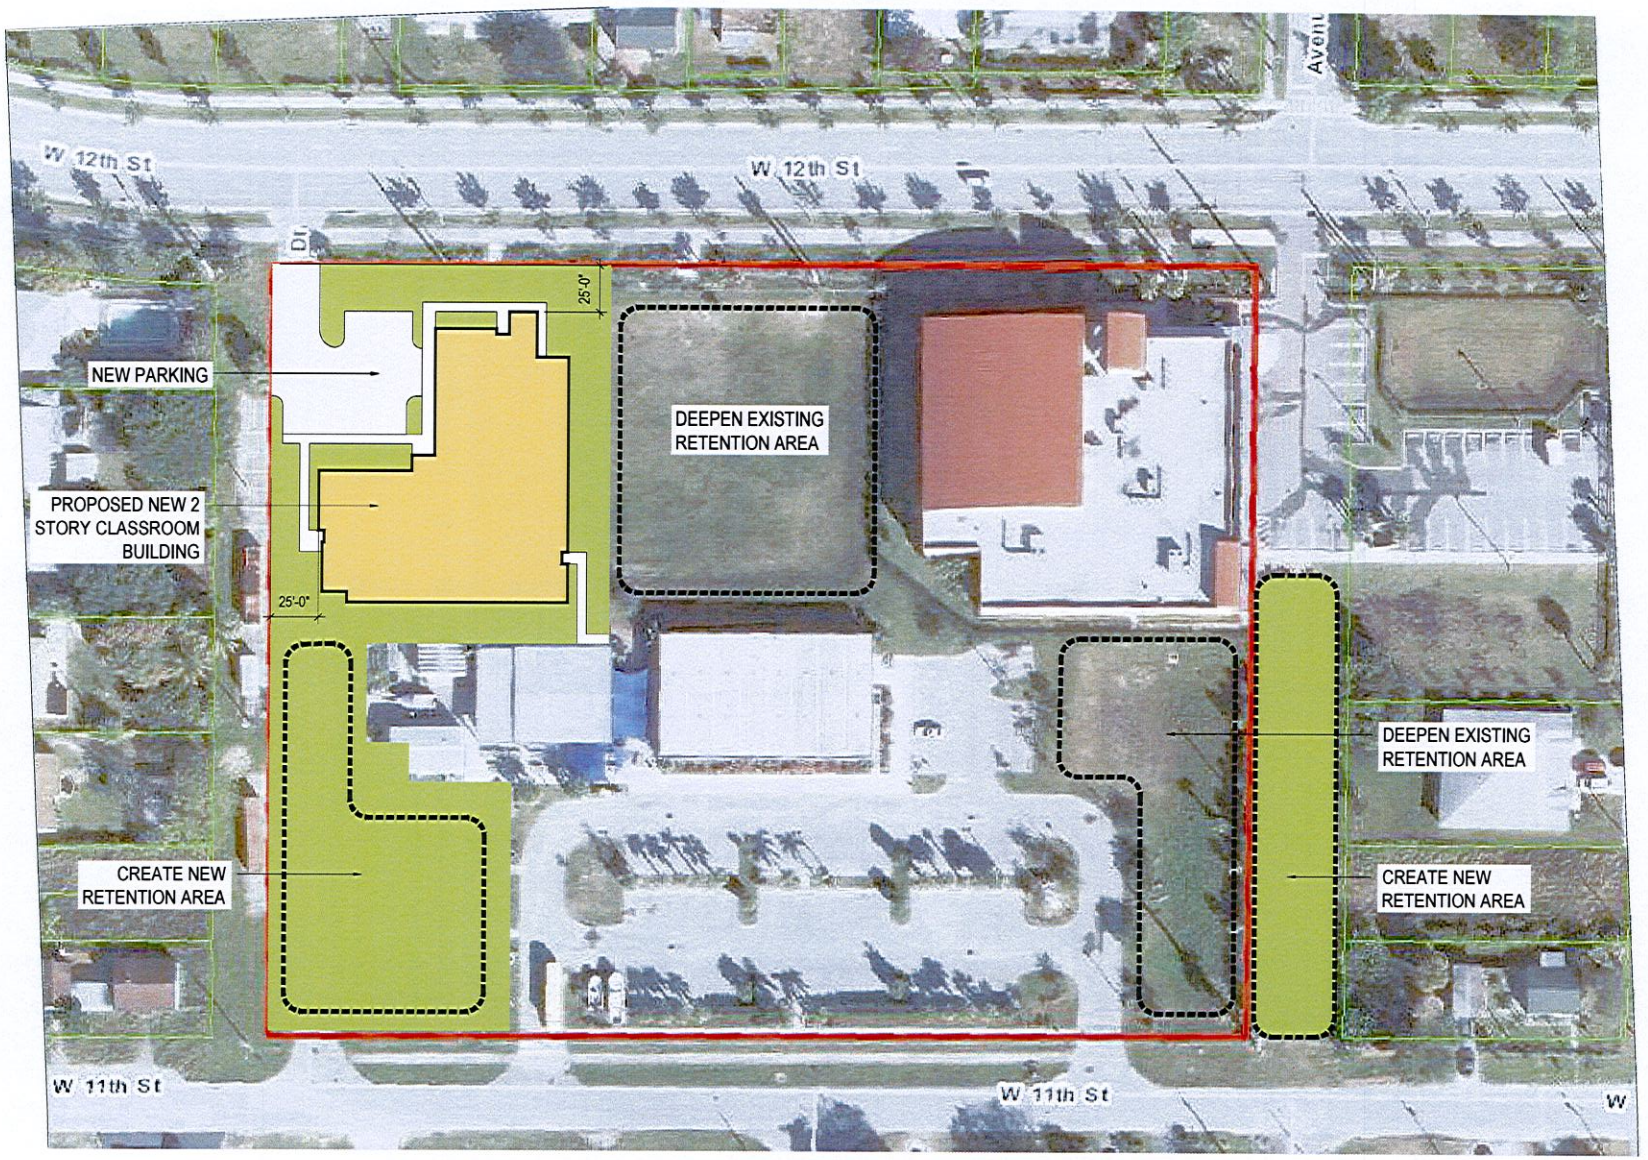



01 CONCEPT SITE PLAN

SCALE: 1"=30'-0"


tercilla coutemanche architects
AA 0003414
2047 vista parkway, suite 100
west palm beach, florida 33411 ph: 561.478.4457 fx: 561.478.4102


NEW CLASSROOM BUILDING
RIVIERA BEACH
MARITIME ACADEMY
RIVIERA BEACH, FLORIDA


| | |
|---|---|
| commission | X |
| date: | 4-7-14 |
| revision | date |
| no. | |

drawing G1



copyright 2014

THE CONTENTS OF THESE DOCUMENTS, INCLUDING BUT NOT LIMITED TO THE DESIGN ARE COPYRIGHTED AND PROPRIETARY. THE ARCHITECT SHALL USE ALL LEGAL MEANS AVAILABLE TO PROTECT SAID COPYRIGHT. ANY USE NOT AUTHORIZED IN WRITING BY THE ARCHITECT IS PROHIBITED.

René Tercilla AIA, REFP

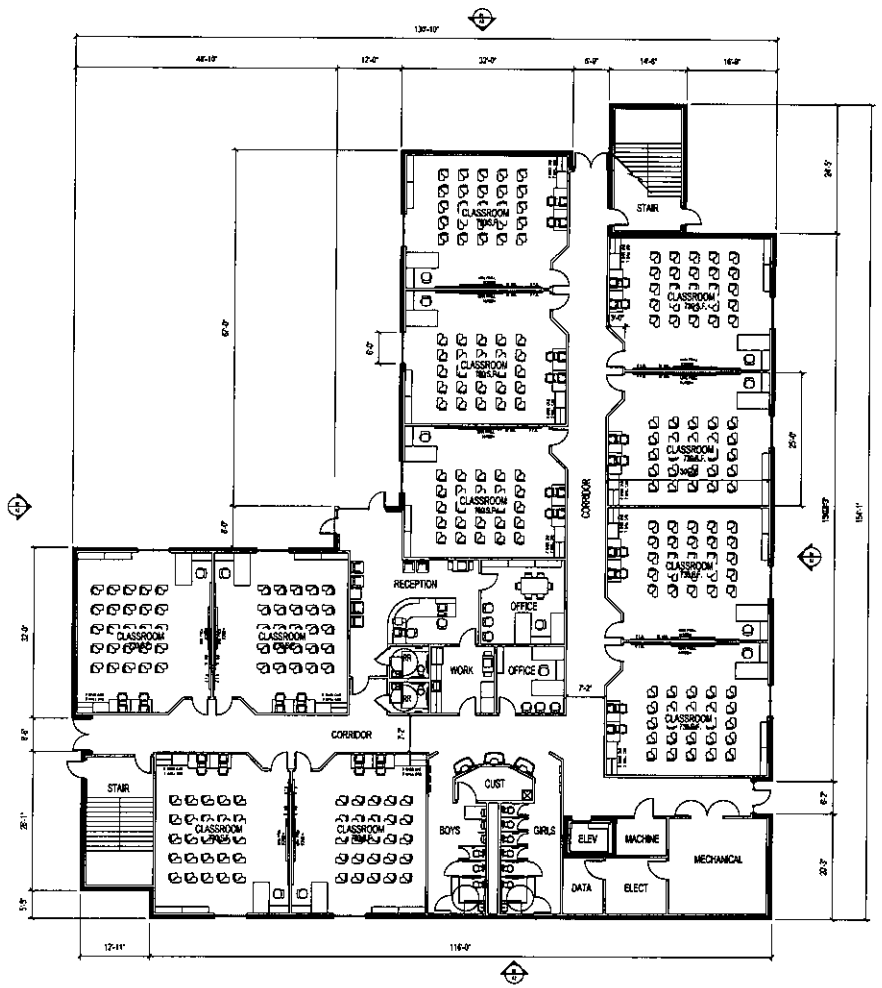


1st FLOOR PLAN

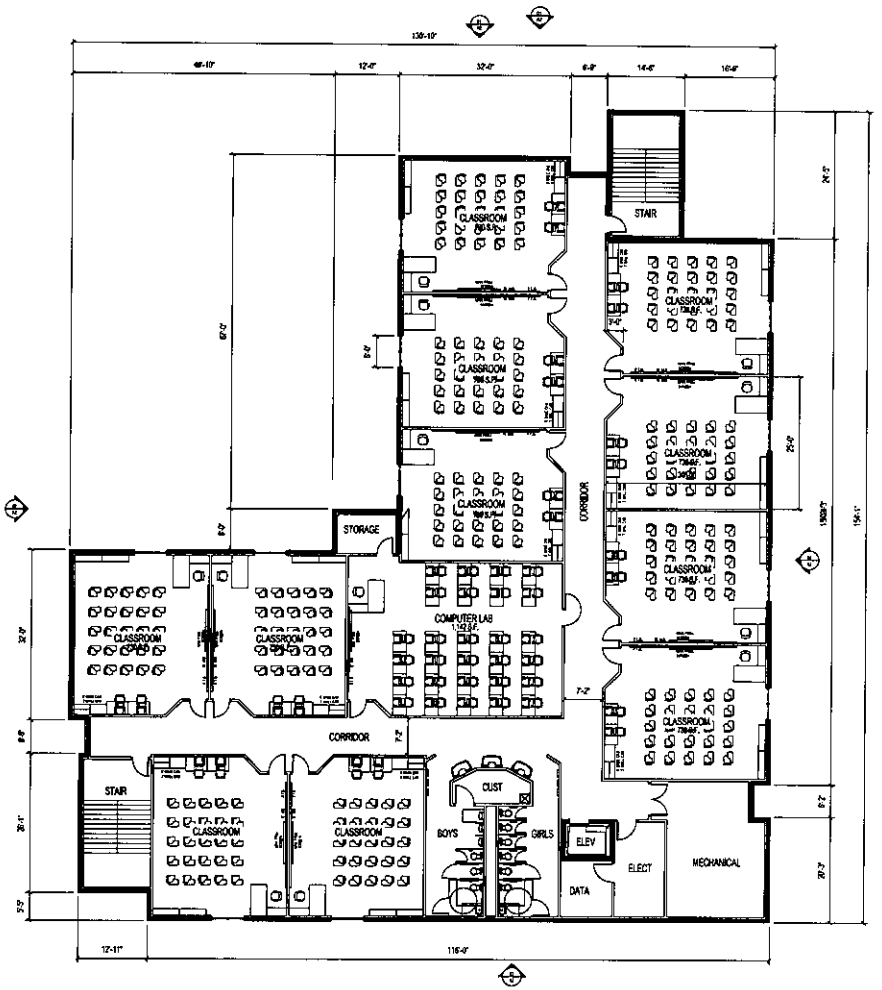


2nd FLOOR PLAN

AREA TABULATION

1ST FLOOR = 14,190 GSF
2ND FLOOR = 13,432 GSF
TOTAL GSF = 27,622 GSF


tercilla courtemanche architects
AA 0003414
2047 vista parkway, suite 100
west palm beach, florida 33411 ph: 561.478.4457 fx: 561.478.1102


NEW CLASSROOM BUILDING
RIVIERA BEACH
MARITIME ACADEMY
RIVIERA BEACH, FLORIDA

| | |
|---|---|
| commission | X |
| date: | 4-7-14 |
| revision | date |
| no. | |

drawing

A1


copyright 2014

THE ARCHITECTURAL WORK DEPICTED HEREIN IS AND SHALL REMAIN THE PROPERTY OF THE ARCHITECT WHETHER THE PROJECT FOR WHICH IT IS PREPARED IS EXECUTED OR NOT. ALL COPYRIGHTS IN SUCH ARCHITECTURAL WORK ARE RESERVED BY THE ARCHITECT. ANY USE OR PUBLICATION WITHOUT THE WRITTEN PERMISSION OF THE ARCHITECT IS PROHIBITED.

René Tercilla AIA, REFP

tercilla *courtemanche* architects, inc.

The Weitz Company




North Elevation

tercilla *courtemanche* architects, inc.

The Weitz Company



East Elevation

tercilla *courtemanche* architects, inc.


The Weitz Company



South Elevation


tercilla *courtemanche* architects, inc.
The Weitz Company
West Elevation

| Act ID | Description | Duration | Early Start | Early Finish |
|---|---|---|---|---|
| **PRE-APPROVAL PHASE** | | | | |
| 030 | VIKIING PROVIDES LIMITED NTP to WEITZ | 0 | 04/14/14 | |
| 010 | Schematic Architecture/programing | 10 | 04/14/14 | 04/25/14 |
| 020 | Civil schematic design | 10 | 04/14/14 | 04/25/14 |
| 040 | MEP schematic design | 10 | 04/14/14 | 04/25/14 |
| 0095 | Conceptual Site Plan Design | 25 | 04/14/14 | 05/16/14 |
| 0091 | WEITZ TO PROVIDE GMP | 10 | 04/28/14 | 05/09/14 |
| 0044 | VIKING REVIEW/APPROVE | 5 | 05/12/14 | 05/16/14 |
| 0071 | NTP to 100% CD and Site Plan approval | 0 | 05/19/14 | |
| **PERMITTING** | | | | |
| 0134 | Revise Final Plans per Conditions of Approval | 10 | 04/14/14 | 04/25/14 |
| 0085 | Soil Borings / Geotechnical Study & Report | 5 | 05/13/14 | 05/19/14 |
| 0072 | Submit Site Plan to City of Riviera Beach | 0 | 05/20/14 | |
| 0082 | City Application Review | 20 | 05/20/14 | 06/17/14 |
| 0092 | Respond & Resubmit to City | 10 | 06/18/14 | 07/01/14 |
| 0002 | Submit Civil Design to CITY | 40 | 06/25/14 | 08/20/14 |
| 0069 | Submit for SFWMD Permit | 66 | 06/30/14 | 10/01/14 |
| 0102 | City Re-Review Application | 20 | 07/02/14 | 07/30/14 |
| 0112 | Respond & Resubmit to City | 7 | 07/31/14 | 08/08/14 |
| 0058 | Submit building permit | 25 | 08/07/14 | 09/11/14 |
| 0122 | City: Re-Review & Certify Application | 10 | 08/11/14 | 08/22/14 |
| 0079 | Obtain Civil Design Approval from CITY | 0 | | 08/20/14 |
| 0132 | CITY Certification/approval of site plan | 0 | | 08/22/14 |
| 0084 | CITY Council Mtg | 1 | 08/25/14 | 08/25/14 |
| 0123 | City Staff Reports | 15 | 08/25/14 | 09/15/14 |
| 0073 | Obtain Site Plan Approval | 0 | | 08/27/14 |
| 0070 | Obtain SFWMD Permit | 0 | | 10/01/14 |
| 0009 | Obtain Building Permit | 0 | | 10/02/14 |
| **DESIGN & GMP** | | | | |
| 0001 | Prepare Civil Design Drawings | 25 | 05/20/14 | 06/24/14 |
| 0006 | Prepare Design Development Drawings (DD) | 25 | 05/20/14 | 06/24/14 |
| 0045 | VIKING Review & Approve DD set | 5 | 06/25/14 | 07/01/14 |
| 0046 | Prepare 100% Construction Documents (CD) | 25 | 07/02/14 | 08/06/14 |
| **CONSTRUCTION** | | | | |
| **SITE WORK** | | | | |
| 0014 | Layout site and buildings | 5 | 10/02/14 | 10/08/14 |
| 0066 | Dig/Fill detention areas | 15 | 10/02/14 | 10/22/14 |

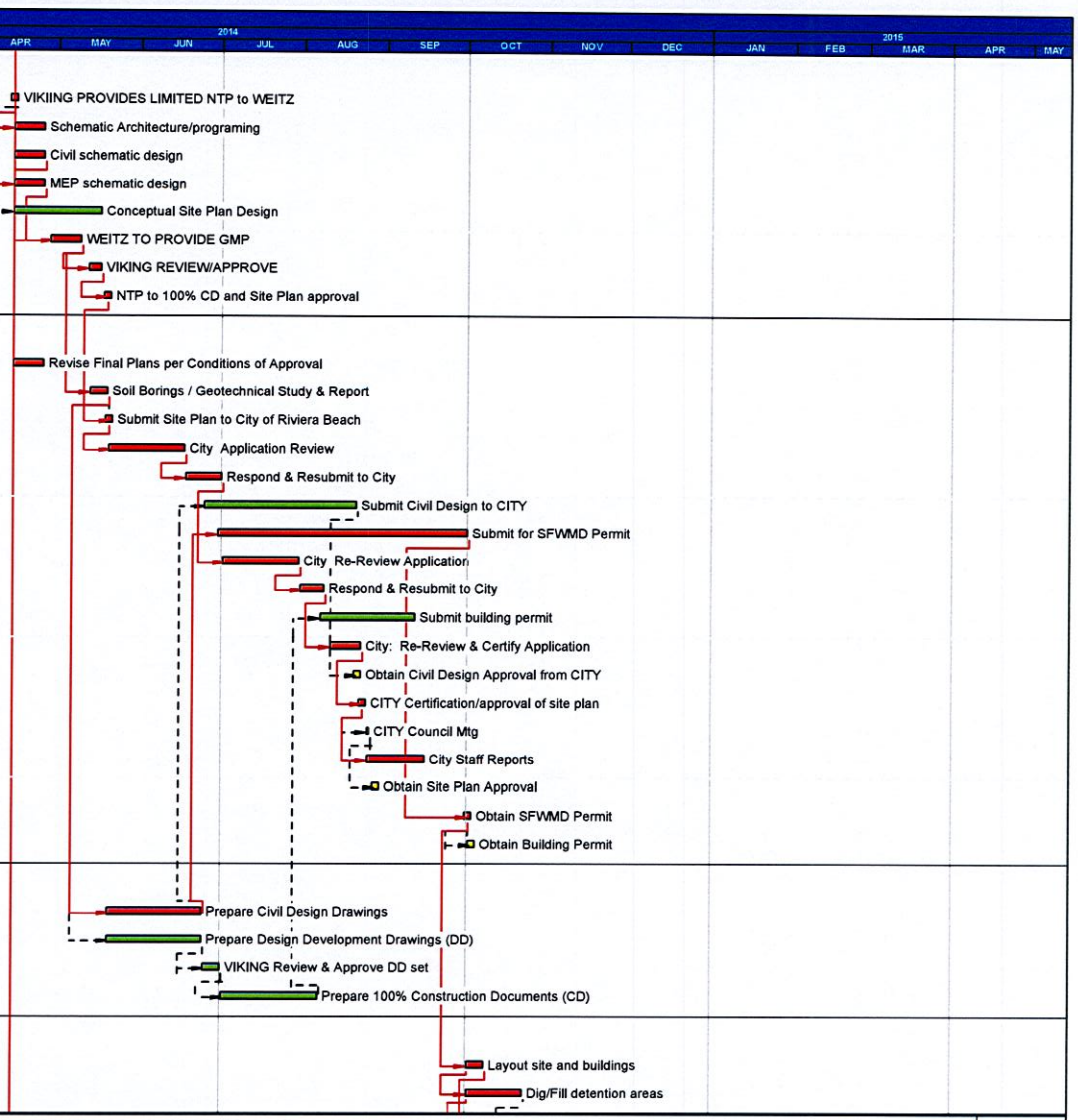



| | |
|---|---|
| Start date | 04/14/14 |
| Finish date | 05/07/15 |
| Data date | 04/14/14 |
| Run date | 04/08/14 |
| Page number | 1A |

© Primavera Systems, Inc.

**Riviera Beach Maritime Academy**
**THE WEITZ COMPANY**

WEITZ

| Act ID | Description | Duration | Early Start | Early Finish |
|---|---|---|---|---|
| 0048 | START OF NEW CONSTRUCTION | 0 | 10/09/14 | |
| 0076 | Underground Utilities & Site Drainage | 20 | 10/23/14 | 11/19/14 |
| 0038 | Site Electrical Rough | 15 | 11/20/14 | 12/12/14 |
| 0037 | Stabilize Parking Lots and Drive Areas | 15 | 12/15/14 | 01/06/15 |
| 0074 | Curb and Gutter | 10 | 01/07/15 | 01/20/15 |
| 0039 | Parking Lot Base Paving | 15 | 01/21/15 | 02/10/15 |
| 0041 | Site MEP Trim Out | 10 | 02/11/15 | 02/24/15 |
| 0077 | Hardscape & Site Amenities | 20 | 02/11/15 | 03/10/15 |
| 0075 | Parking Lot Second Lift Paving & Striping | 10 | 03/11/15 | 03/24/15 |
| 0040 | Irrigation and Landscaping | 20 | 03/25/15 | 04/21/15 |
| NEW BUILDING | | | | |
| 0059 | | 1 | 04/14/14 | 04/14/14 |
| 0089 | | 1 | 04/14/14 | 04/14/14 |
| 0018 | Prepare Building Pad | 4 | 10/09/14 | 10/14/14 |
| 0015 | Foundations | 7 | 10/15/14 | 10/23/14 |
| 0016 | U/G MEP Rough-In | 10 | 10/29/14 | 11/11/14 |
| 0017 | Form and Pour Slab-On-Grade | 5 | 11/05/14 | 11/11/14 |
| 0019 | Form and Pour Concrete Panels | 10 | 11/12/14 | 11/25/14 |
| 0020 | Erect Concrete Panels | 10 | 11/19/14 | 12/04/14 |
| 0021 | Erect Structural Steel & Deck | 10 | 11/26/14 | 12/11/14 |
| 0022 | MEP Rough-In at Elevated Deck | 5 | 12/11/14 | 12/17/14 |
| 0023 | Pour Elevated Concrete Deck | 5 | 12/18/14 | 12/24/14 |
| 0025 | Install Exterior Glass & Glazing | 10 | 12/26/14 | 01/09/15 |
| 0024 | Install Roof / Dry-In | 12 | 12/31/14 | 01/16/15 |
| 0027 | Overhead MEP Rough-In | 16 | 01/08/15 | 01/29/15 |
| 0064 | Roof Detailing | 10 | 01/19/15 | 01/30/15 |
| 0026 | Exterior Panel Texture | 5 | 01/26/15 | 01/30/15 |
| 0028 | Wall Framing | 10 | 02/05/15 | 02/18/15 |
| 0029 | Wall MEP Rough-In | 10 | 02/19/15 | 03/04/15 |
| 0030 | Hang and Finish Drywall | 12 | 03/05/15 | 03/20/15 |
| 0031 | Prime / Paint | 5 | 03/16/15 | 03/20/15 |
| 0032 | Acoustical Ceiling Grid | 8 | 03/23/15 | 04/01/15 |
| 0033 | MEP Ceiling Drops / Wall Trim Out | 8 | 03/30/15 | 04/08/15 |
| 0034 | Install VCT | 8 | 04/13/15 | 04/22/15 |
| 0035 | Drop Ceiling Tile | 6 | 04/16/15 | 04/23/15 |
| 0080 | Trimout | 5 | 04/24/15 | 04/30/15 |
| 0042 | Final Inspections | 5 | 05/01/15 | 05/07/15 |
| 0049 | Substantial Completion | 0 | 05/08/15 | |

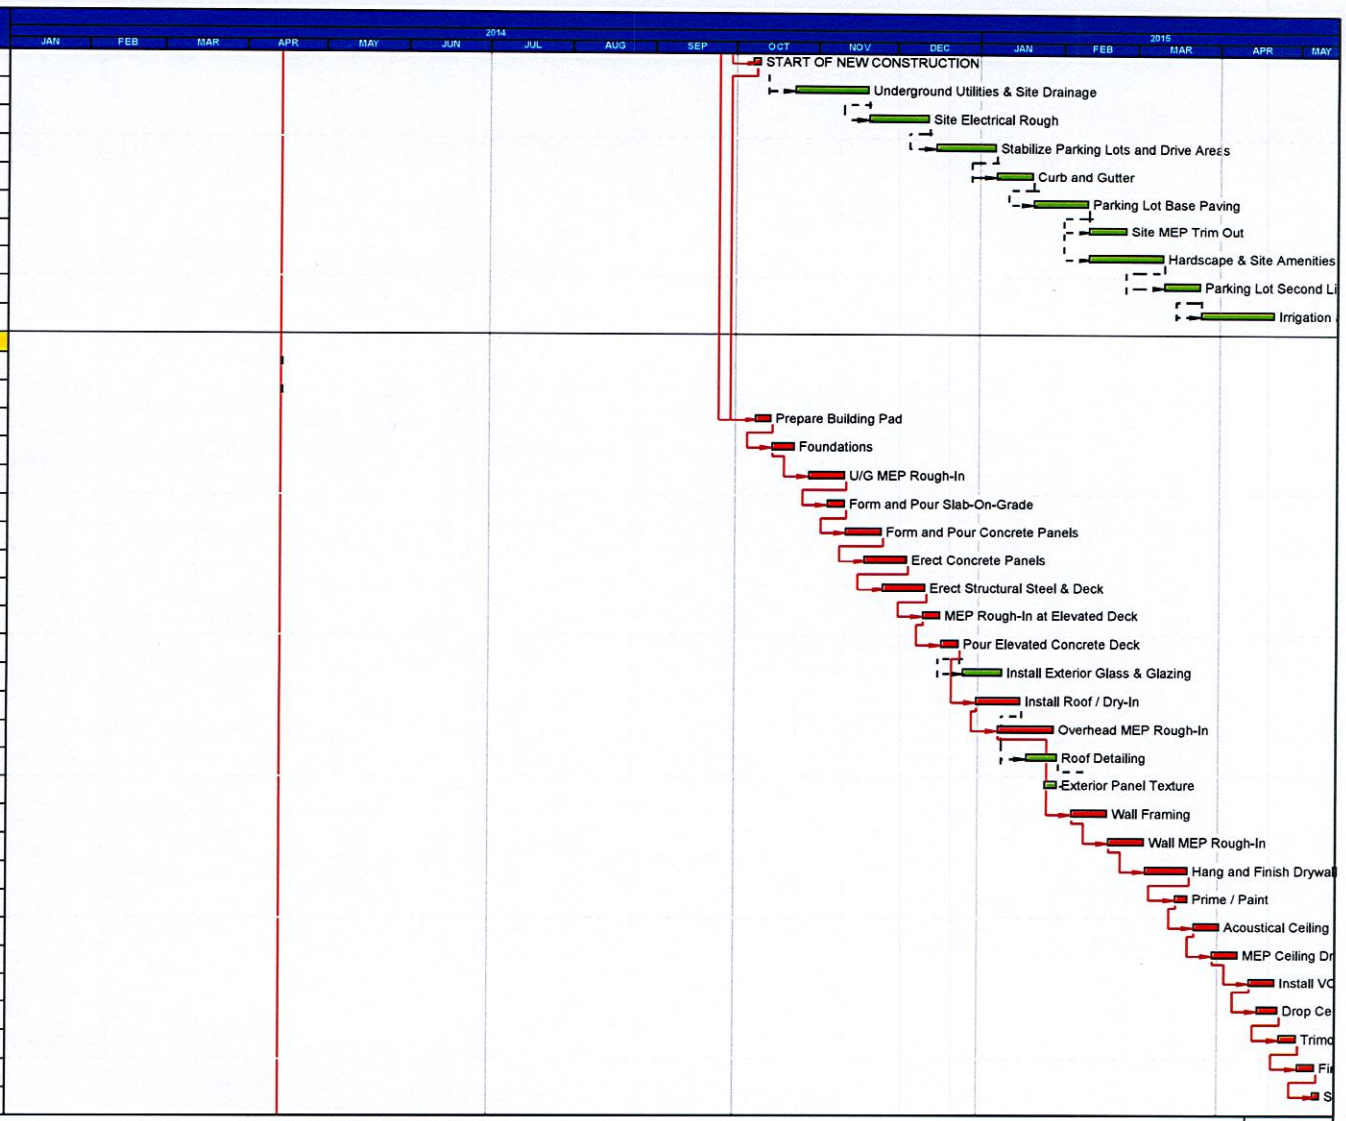


| | |
|---|---|
| Start date | 04/14/14 |
| Finish date | 05/07/15 |
| Data date | 04/14/14 |
| Run date | 04/08/14 |
| Page number | 2A |

© Primavera Systems, Inc.

**Riviera Beach Maritime Academy**
**THE WEITZ COMPANY**
